


TO BE COMPLETED BY SW360									
SW360 PRODUCT CODE :									
MEDIA TYPE (CIRCLE ONE) :	PERLITE	ZPG	OTHER:						
CARTRIDGE QTY (STATE) :	PRE-INSTALLATION (Y/N):								
SP FLOW RATE (CIRCLE ONE):	FULL (Ø 27.6 ID) BLACK/MUSTARD	3 QTR (Ø 24.0 ID) WHITE/OPAL	HALF (Ø 19.7 ID) GREEN	OTHER:					
ACCESS COVER (CIRCLE ONE) :	ALLOY CHE	QUER PLATE	OTHER:						
COMPLETED BY:	SIGNED:		DATE:						

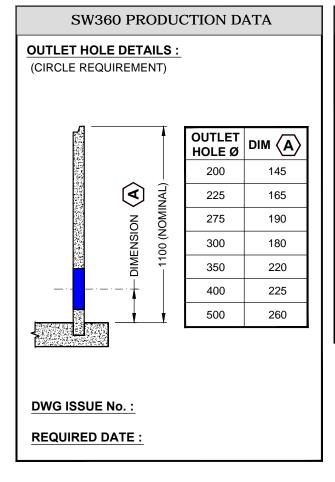

NOTES

- MANHOLE UNIT FITTED WITH SWIFTLIFT ANCHOR POINTS (QTY 2). DO NOT EXCEED 60 DEGREE LIFT ANGLE.
- UNIT SUPPLIED WITH OUTLET CORE DRILLED. INLET/S CORE DRILLED ON SITE BY OTHERS WITHIN RANGE SHOWN ON DRAWING.
- SEALING / GROUTING OF MANHOLE COMPONENTS AND PIPES BY CONTRACTOR. ENSURING LOCAL CODES AND REGULATIONS ARE COMPLIED WITH.
- ANY RISERS REQUIRED TO INCREASE THE DEPTH TO INVERT (DTI) FROM THAT AS DRAWN TO BE SUPPLIED BY THE CONTRACTOR.
- FOR A DTI EXCEEDING 5m PLEASE CONTACT 0800STORMWATER
- CONTRACTOR TO TAKE APPROPRIATE MEASURES TO PROTECT
- CARTRIDGES FROM CONSTRUCTION RELATED EROSION RUNOFF. BACKFILL, BEDDING AND BUOYANCY DESIGN BY ENGINEER OF
- QTY OF CARTRIDGES BY ENGINEER OF RECORD.
- CONCRETE MANHOLE RISERS ARE DESIGNED AND MANUFACTURED IN ACCORDANCE WITH AS/NZS 4058: 2007
- CONCRETE MANHOLE BASES ARE DESIGNED AND MANUFACTURED IN ACCORDANCE WITH NZS 3101 : 2006 & NZS 3109 : 1997
- 11. ALUMINIUM LID / NON-TRAFFICABLE
- 12. FOR REQUIREMENTS OUTSIDE OF DRAWING SPECIFICATIONS PLEASE CONTACT 0800STORMWATER.

APPROX WEIGHTS

MANHOLE SECTION INCLUDING CARTRIDGES: 2550 Kg (AS DELIVERED, BASED ON QTY 4 ZPG CARTS)



CONDITION OF USE 0800 STORMWATER © STORMWATER360 2019 sales@stormwater360.co.nz Any unauthorised reproduction of this drawing in part or in full is prohibited www.stormwater360.co.nz

SCALE: NTS

STORMFILTER® CARTRIDGE FILTRATION SYSTEM 69cm CART / DN1500 x 1200 MH : NON - TRAFFICABLE **GENERAL ARRANGEMENT** DRG No: SF-MH-69-1500-NT-20 | REV: 1 | DATE: 01.03.19

JOB NO:				REV	REVISION DETAIL	DATE
PROJECT:				0	APPROVED	01.03.1
				1	MARK-UPS	09.04.1
DRN:	R.P.		01.03.19			
CKD:	G.S.	G.Y.	01.03.19			
